



END-TO-END PROJECT PROCESS: INTAKE TO EXIT

An end-to-end pathway from intake, assessment and investment preparation to delivery, handover and close-out.





UNITED AFRIKA
CHAMBER OF COMMERCE
(UACOC)
Pan-African Trade • Investment • Enterprise Development

PROJECT SUBMISSION PROCESS MAP

The Project Submission process captures project opportunities in a consistent format, establishes an official record, identifies the submitting party, and determines whether the submission is sufficiently complete to proceed to registration and screening.

PROCESS KEY



Note: This process map is aligned with the Project Submission detailed process described in the *Project Submission Process Guide*.



PROJECT REGISTRATION PROCESS MAP

The Project Registration process creates the official project identity and record, classifies the project, assigns governance attributes, and activates the next lifecycle stage.

PROCESS KEY

Start

End

Process Flow

Decision Flow

Decision Point

Key Output



PROJECT REGISTRATION CONTROL POINTS

- ✓ Authorised personnel
- ✓ Accepted-submission verification
- ✓ Duplicate-project check
- ✓ Unique registration number
- ✓ Mandatory registration fields
- ✓ Classification control
- ✓ Confidentiality classification
- ✓ Project-officer assignment
- ✓ Audit-trail activation
- ✓ Data-quality review

KEY OUTPUTS

- 📄 Official registration number
- 📄 Project-register entry
- 📄 Approved project name
- 📄 Lifecycle stage
- 📄 Administrative status
- 📄 Category classification
- 📄 Size / priority classification
- 📄 Initial risk flag record
- 📄 Confidentiality classification
- 📄 Assigned project officer
- 📄 Electronic project file
- 📄 Registration summary
- 📄 Registration approval
- 📄 Sponsor notification
- 📄 Activated dashboard / audit trail

RESPONSIBILITY MATRIX

ROLE	RECORD CREATION	CLASSIFICATION & ATTRIBUTES	VALIDATION & CONTROL	APPROVAL & ACTIVATION
Registration Officer	R	R	R	
Intake Officer	R			
Records Administrator	R		R	
Project Officer		R	R	
Portfolio Manager		R		
Compliance Officer			R	
System Administrator		R		R
Approving Authority				R
Project Sponsor				R

ENTRY CRITERIA

- ✓ Accepted submission received
- ✓ Quality review passed
- ✓ Accepted for registration
- ✓ Sponsor / project identifiable
- ✓ Minimum information available
- ✓ Registration officer has submission package

EXIT CRITERIA

- ✓ Project entered into official register
- ✓ Unique registration number assigned
- ✓ Official identity established
- ✓ Project classified
- ✓ Lifecycle stage and status assigned
- ✓ Responsible unit and project officer appointed
- ✓ Initial risks and outstanding information recorded
- ✓ Project file created

Note: This process map is aligned to the detailed Project Registration process manual and supporting governance framework.



UNITED AFRIKA
CHAMBER OF COMMERCE
(UACOC)

Pan-African Trade • Investment • Enterprise Development

SPONSOR AND OWNERSHIP VERIFICATION PROCESS MAP

The Sponsor and Ownership Verification process confirms the legal identity, authority, ownership structure, beneficial ownership, project rights, governance standing and delivery capacity of the project sponsor and all relevant project parties.

PROCESS KEY



PROJECT CONTROL POINTS

- ✓ Identity verification completed
- ✓ Authority to act confirmed
- ✓ Legal entities verified
- ✓ Beneficial ownership disclosed
- ✓ Project rights validated
- ✓ Capacity assessment completed
- ✓ All documents reviewed
- ✓ Risk disclosures recorded
- ✓ Declarations confirmed
- ✓ Quality check passed

KEY OUTPUTS

- 📄 Verified Sponsor Profile
- 📄 Ownership Structure Report
- 📄 Verification Findings Report
- 📄 Beneficial Ownership Register
- 📄 Project Rights Confirmation
- 📄 Sponsor Capacity Profile
- 📄 Risk Disclosure Summary
- 📄 Verification Approval Record
- 📄 Supporting Documents Index
- 📄 Verification Outcome Report

RESPONSIBILITY MATRIX (R)

ACTIVITY	VERIFICATION OFFICER	LEGAL ADVISER	COMPLIANCE OFFICER	PROJECT OFFICER	QUALITY REVIEWER
1 – 5 Identity & Entity Verification	R	R			
6 – 9 Compliance & Rights Verification	R		R		
10 – 14 Capacity & Risk Assessment	R			R	
15 – 18 Documentation & Validation		R			
19 – 21 Submission & Record Creation	R			R	
22 – 23 Quality Decision & Outcome			R		R

ENTRY CRITERIA

- ✓ Project registered
- ✓ Unique registration number issued
- ✓ Sponsor and parties identified
- ✓ Initial documents submitted
- ✓ Verification officer assigned
- ✓ Status set to: Pending Verification


EXIT CRITERIA

- ✓ Identity and authority verified
- ✓ Ownership and rights confirmed
- ✓ Compliance and capacity assessed
- ✓ All supporting documents validated
- ✓ Quality standards met
- ✓ Status updated to: Verified – Ready for Screening



MINIMUM-INFORMATION REVIEW PROCESS MAP

The Minimum-Information Review process evaluates whether a registered and integrity-cleared project contains the essential information required to enter Classification, Prioritisation and Detailed Assessment. It ensures information sufficiency, quality and integrity across all key project domains.

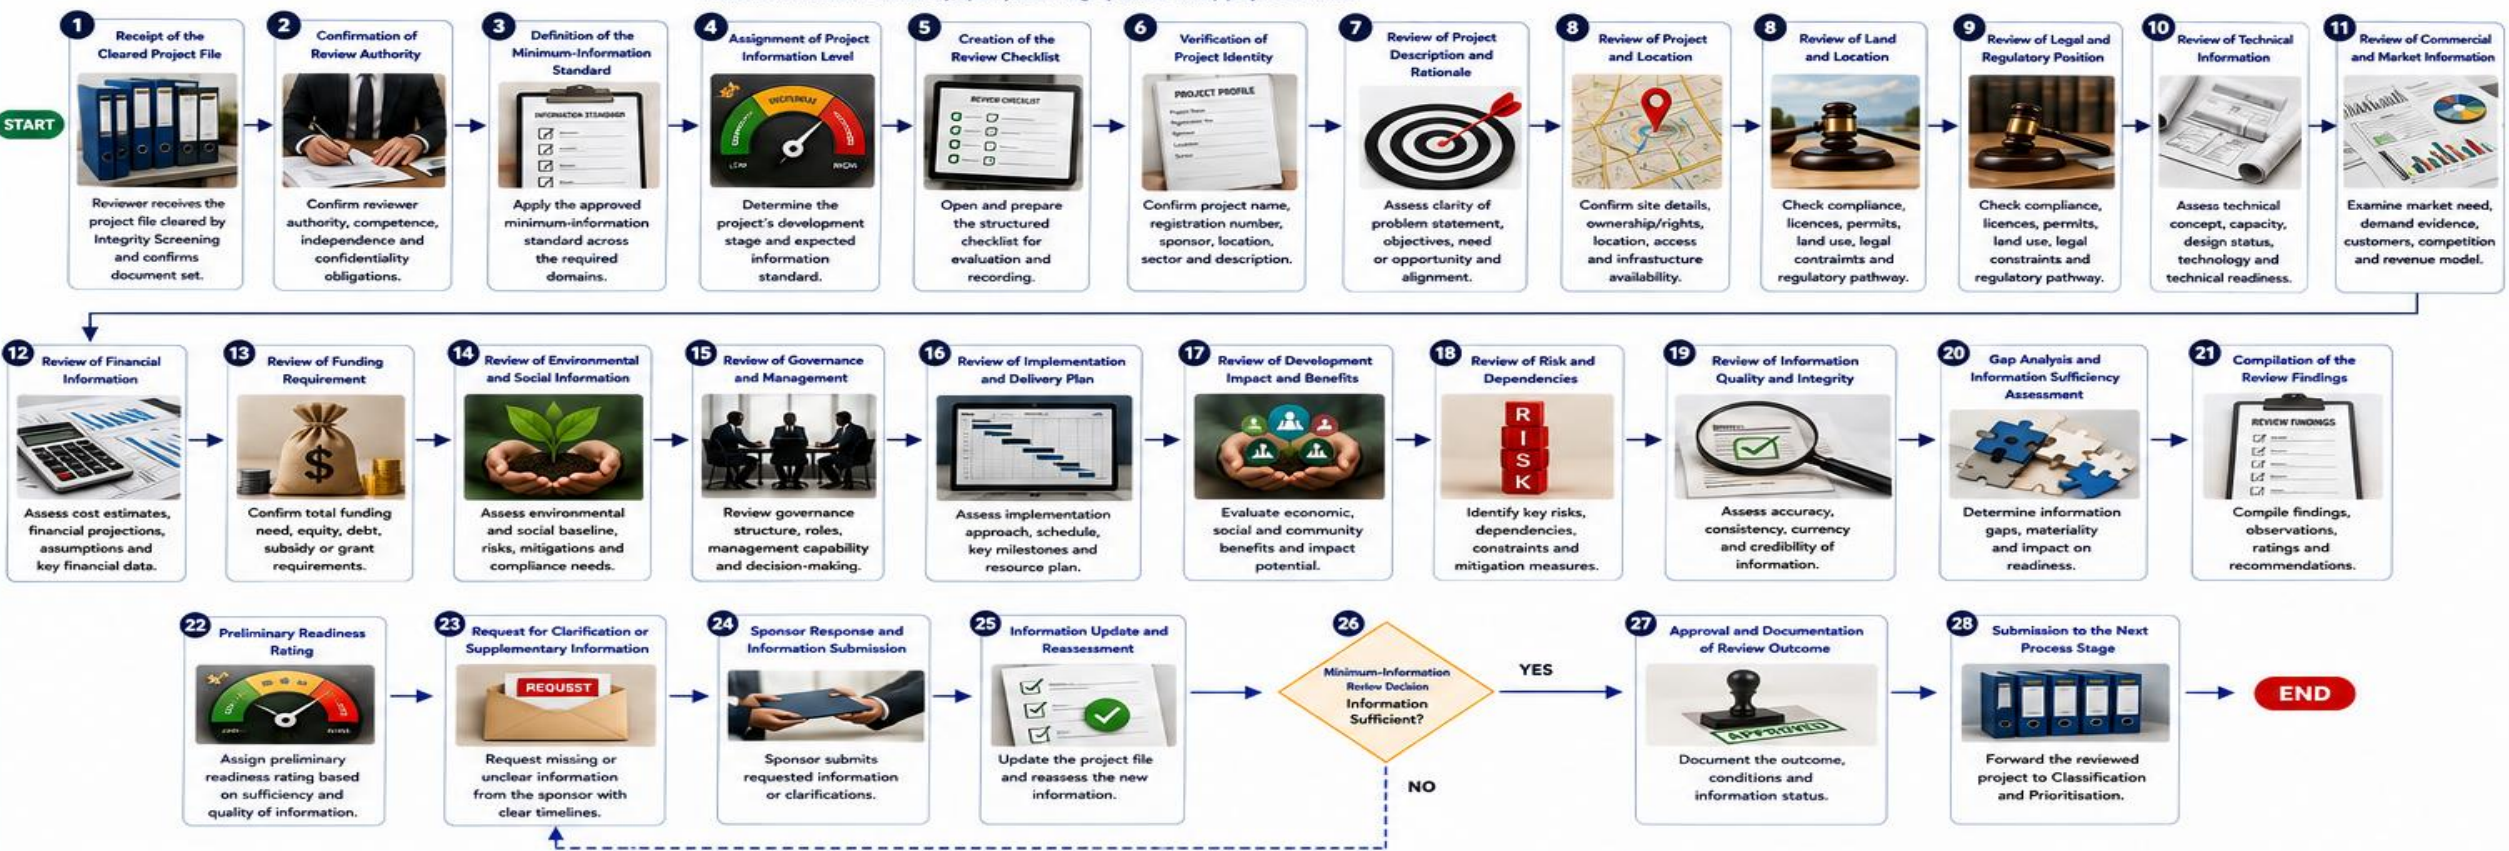

MINIMUM-INFORMATION REVIEW CONTROL POINTS	KEY OUTPUTS	RESPONSIBILITY MATRIX (R)							ENTRY CRITERIA	EXIT CRITERIA																																																		
✓ Authority and independence confirmed ✓ Standard applied consistently ✓ All required domains reviewed ✓ Information quality assessed ✓ Gaps identified and recorded ✓ Readiness rated appropriately ✓ Decisions documented ✓ Audit trail maintained ✓ Confidentiality protected ✓ Escalations managed	📄 Completed review checklist 📄 Information sufficiency assessment 📄 Gap analysis report 📄 Preliminary readiness rating 📄 Review findings report 📄 Information request log (if applicable) 📄 Review decision record 📄 Updated project file 📄 Referral to next process stage	<table><thead><tr><th>ACTIVITY</th><th>REVIEWER</th><th>TECHNICAL SPECIALIST</th><th>RISK & LEGAL SPECIALIST</th><th>FINANCIAL ANALYST</th><th>QUALITY REVIEWER</th><th>APPROVING AUTHORITY</th></tr></thead><tbody><tr><td>1 – 5 Initiate Review</td><td>R</td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>6 – 11 Domain Reviews A – G</td><td>R</td><td>R</td><td></td><td></td><td></td><td></td></tr><tr><td>12 – 17 Domain Reviews H – J</td><td>R</td><td></td><td>R</td><td>R</td><td></td><td></td></tr><tr><td>18 – 20 Risk, Quality & Sufficiency</td><td>R</td><td></td><td>R</td><td></td><td></td><td></td></tr><tr><td>21 – 25 Gap Management & Update</td><td>R</td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>26 – 28 Decision & Submission</td><td>R</td><td></td><td></td><td></td><td></td><td>R</td></tr><tr><td colspan="7">R = Responsible A = Accountable C = Consulted I = Informed</td></tr></tbody></table>	ACTIVITY	REVIEWER	TECHNICAL SPECIALIST	RISK & LEGAL SPECIALIST	FINANCIAL ANALYST	QUALITY REVIEWER	APPROVING AUTHORITY	1 – 5 Initiate Review	R						6 – 11 Domain Reviews A – G	R	R					12 – 17 Domain Reviews H – J	R		R	R			18 – 20 Risk, Quality & Sufficiency	R		R				21 – 25 Gap Management & Update	R						26 – 28 Decision & Submission	R					R	R = Responsible A = Accountable C = Consulted I = Informed							✓ Project integrity-cleared ✓ Ownership verified (or conditionally verified) ✓ Registered in the system ✓ All submitted documents captured ✓ Reviewer assigned and authorised ✓ Minimum-information standard available ✓ Review resources and tools available	✓ Review completed and documented ✓ Information sufficiency decision made ✓ Information gaps addressed or recorded ✓ Readiness rating assigned ✓ Review findings approved ✓ Project submitted to next stage ✓ Audit trail complete
ACTIVITY	REVIEWER	TECHNICAL SPECIALIST	RISK & LEGAL SPECIALIST	FINANCIAL ANALYST	QUALITY REVIEWER	APPROVING AUTHORITY																																																						
1 – 5 Initiate Review	R																																																											
6 – 11 Domain Reviews A – G	R	R																																																										
12 – 17 Domain Reviews H – J	R		R	R																																																								
18 – 20 Risk, Quality & Sufficiency	R		R																																																									
21 – 25 Gap Management & Update	R																																																											
26 – 28 Decision & Submission	R					R																																																						
R = Responsible A = Accountable C = Consulted I = Informed																																																												

NOTE: The Minimum-Information Review is a controlled information-gate assessment. It does not confirm feasibility, bankability or investment approval.



INTEGRITY SCREENING PROCESS MAP

The Integrity Screening process evaluates the ethical, legal, regulatory and reputational standing of the project sponsor, beneficial owners, directors, related parties and other connected persons or entities to identify unacceptable risks and ensure responsible institutional engagement.



INTEGRITY SCREENING CONTROL POINTS

- ✓ Identity data verified
- ✓ Sanctions screening completed
- ✓ PEP and control screening done
- ✓ Adverse media reviewed
- ✓ Legal and regulatory checks done
- ✓ Conflicts of interest reviewed
- ✓ Source of funds assessed
- ✓ Integrity risk scored
- ✓ Findings documented
- ✓ Decision approved
- ✓ Outcome recorded

KEY OUTPUTS

- Screening Scope Report
- Sanctions Screening Report
- PEP and Control Report
- Adverse Media Report
- Legal and Regulatory Report
- Integrity Risk Assessment
- Screening Findings Report
- Integrity Recommendation
- Integrity Decision Record
- Notification Letter
- Updated Lifecycle Status

RESPONSIBILITY MATRIX (R)

ACTIVITY	SCREENING OFFICER	LEGAL / COMPLIANCE	RISK / AML	INTEGRITY MANAGER	QUALITY REVIEWER
1 - 6 Identity & Business Verification	R				
7 - 9 Sanctions, PEP & Media Screening	R		R		
10 - 14 Legal, Regulatory Risk Review	R	R			
15 - 16 Risk Scoring & Repeat Controls	R				
17 - 18 Recommendation Quality fix	R			R	R
19 - 23 Decision, Recording & Notification	R			R	

ENTRY CRITERIA

- ✓ Sponsor & ownership verification completed or conditional
- ✓ Complete identity & ownership information available
- ✓ Project registration number issued
- ✓ Screening officer assigned
- ✓ No immediate disqualifying issues
- ✓ Screening scope approved

EXIT CRITERIA

- ✓ Integrity risk assessed and decision reached
- ✓ No unacceptable risk outstanding
- ✓ Outcome recorded in the system
- ✓ Sponsor notified
- ✓ Lifecycle status updated
- ✓ Ready for next stage

NOTE: Integrity screening assesses ethical, legal and reputational risk. It does not assess technical feasibility or commercial viability.




**UNITED AFRIKA
CHAMBER OF COMMERCE**
(UACOC)

Pan-African Trade • Investment • Enterprise Development

CLASSIFICATION AND PRIORITISATION PROCESS MAP

The Classification and Prioritisation process categorises the project, ranks its strategic importance and assigns the appropriate processing pathway and priority level.

PROCESS KEY

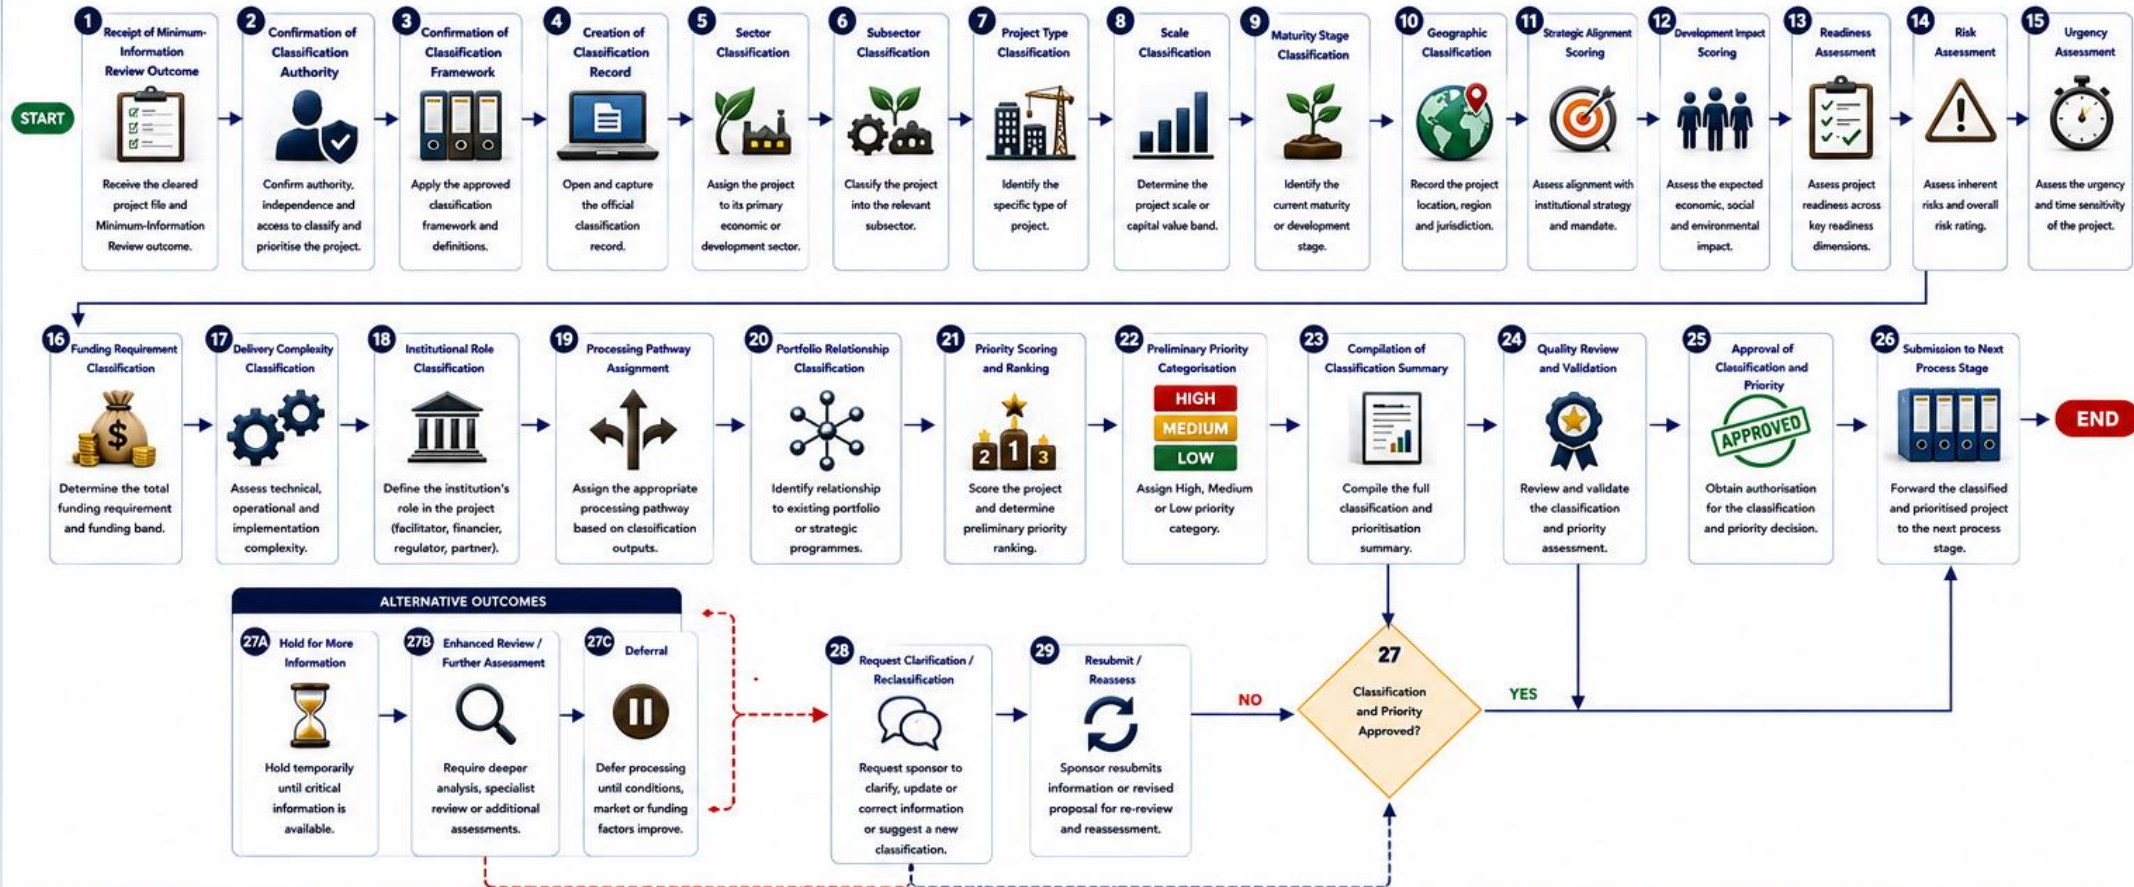

CLASSIFICATION DIMENSIONS

- ✓ Sector & Subsector
- ✓ Project Type
- ✓ Scale / Value
- ✓ Maturity Stage
- ✓ Geographic Location
- ✓ Strategic Alignment
- ✓ Readiness
- ✓ Risk
- ✓ Impact
- ✓ Urgency
- ✓ Funding Requirement
- ✓ Delivery Complexity
- ✓ Institutional Role
- ✓ Processing Pathway
- ✓ Portfolio Relationship
- ✓ Priority Level

KEY OUTPUTS

- 📄 Classification Record
- 📄 Priority Ranking
- 📄 Processing Pathway
- 📄 Classification Summary Report
- 📄 Priority Justification
- 📄 Next Stage Recommendation
- 📄 Audit Trail Entry

RESPONSIBILITY MATRIX (R)

ACTIVITY	CLASSIFICATION OFFICER	PORTFOLIO MANAGER	TECHNICAL SPECIALIST	FINANCIAL ANALYST	QUALITY REVIEWER	APPROVING AUTHORITY
1 – 10 Classification	R	A	C		I	
11 – 20 Assessment & Scoring	R	A	C	C	I	
21 – 26 Prioritisation & Approval	R	A	C	C	R	A
27 – 29 Alternative Outcomes	R	A	C	C	I	

R = Responsible A = Accountable C = Consulted I = Informed

ENTRY CRITERIA

- ✓ Minimum-Information Review approved to proceed
- ✓ Integrity Screening cleared or conditionally cleared
- ✓ Required supporting documents available
- ✓ Information sufficient to classify

EXIT CRITERIA

- ✓ Project classified across all required dimensions
- ✓ Priority level assigned and approved
- ✓ Processing pathway determined
- ✓ Classification record completed
- ✓ Project forwarded to next stage



NOTE: Classification and Prioritisation ensures fair, transparent and strategic allocation of institutional resources and attention.




UNITED AFRIKA CHAMBER OF COMMERCE (UACOC)

Pan-African Trade • Investment • Enterprise Development

PROJECT ONBOARDING PROCESS MAP

This process ensures a structured, transparent and well-governed onboarding of projects into the institutional lifecycle by confirming understanding, establishing governance, and preparing for diagnostic assessment and next-stage activities.

PROCESS KEY

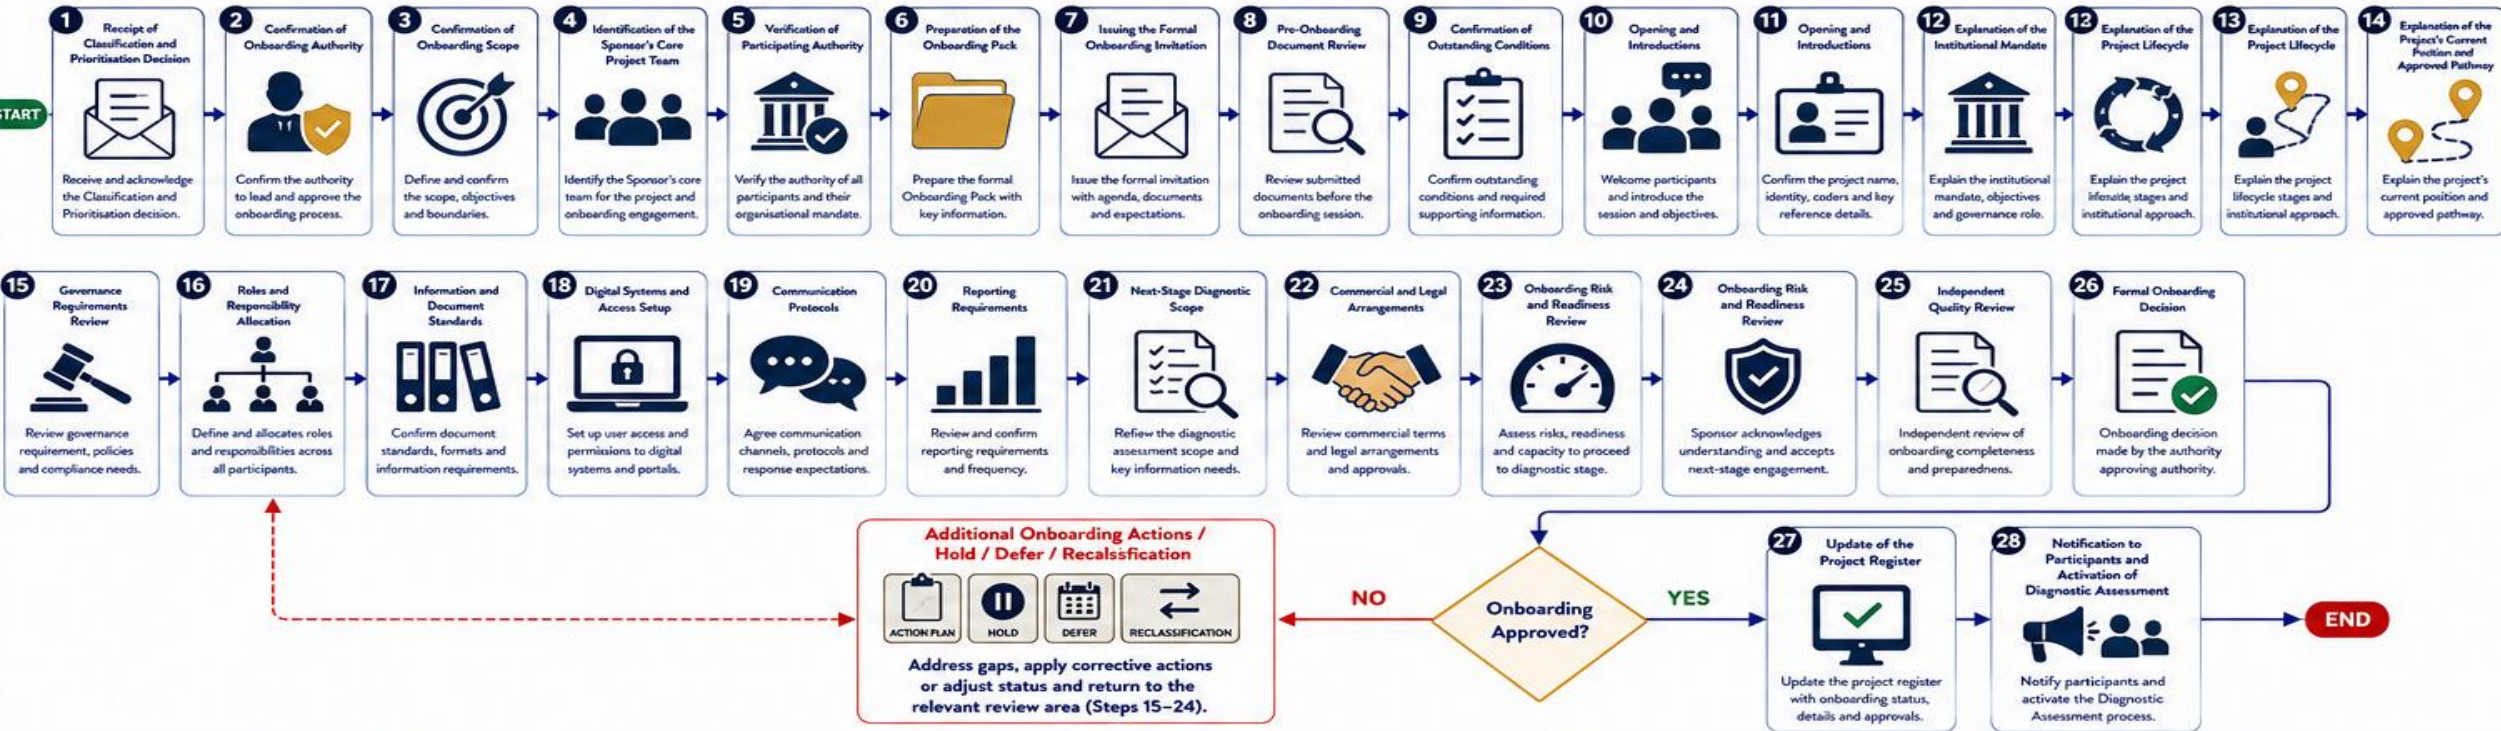

1 ONBOARDING CONTROL POINTS
✓ Authorised entry from Classification and Prioritisation ✓ Verified participation authority ✓ Formal onboarding pack ✓ Mandatory sponsor attendance ✓ Confirmed project identity and status ✓ Governance establishment ✓ Responsibility matrix defined ✓ Communication channels ✓ Document standards ✓ Role-based digital access ✓ Agreed work programme ✓ Condition tracking ✓ Strong record-keeping ✓ Independent quality review ✓ Formal approval ✓ Complete audit trail

2 KEY OUTPUTS
📄 Onboarding invitation and attendance record 📄 Approved onboarding pack 📄 Confirmed sponsor project team 📄 Verified participant authorities 📄 Confirmed project identity and lifecycle status 📄 Documented governance pathway 📄 Approved governance structure 📄 Roles and responsibility matrix 📄 Communication protocol 📄 Reporting framework 📄 Document management protocol 📄 Approved digital-system access 📄 Action register 📄 Condition register 📄 Diagnostic scope 📄 Work programme 📄 Milestones schedule 📄 Onboarding readiness rating 📄 Signed sponsor acknowledgement 📄 Formal onboarding report 📄 Approved onboarding decision 📄 Updated project register 📄 Authorisation to begin Diagnostic Assessment

3 RESPONSIBILITY MATRIX (R)							
ACTIVITY	PROJECT SPONSOR	PROJECT LEAD	ONBOARDING COORDINATOR	LEGAL / COMPLIANCE	RECORDS ADMINISTRATOR	QUALITY REVIEWER	APPROVING AUTHORITY
1–9 Preparation	R	R	R	C	I	I	I
10–20 Session and Protocol Alignment	R	A	R	C	I	I	I
21–24 Work Programme and Sponsor Acknowledgement	A	R	R	C	I	I	I
25–28 Review, Decision and Activation	A	C	R	C	R	R	A
R = Responsible A = Accountable C = Consulted I = Informed							

4 ENTRY CRITERIA
✓ Classification and Prioritisation completed ✓ Priority category assigned ✓ Processing pathway approved ✓ Responsible unit and project lead appointed ✓ Project authorised to proceed ✓ Previous-stage conditions identified ✓ Sponsor and relevant parties available ✓ Onboarding coordinator assigned ✓ Onboarding pack prepared

5 EXIT CRITERIA
✓ Formal onboarding session attended ✓ Project identity, status, priority and pathway confirmed ✓ Institutional mandate and lifecycle explained ✓ Governance arrangements established ✓ Roles and authority documented ✓ Communication and escalation protocols approved ✓ Document standards accepted ✓ Confidentiality and data protection confirmed ✓ Digital access activated ✓ Reporting requirements established ✓ Conditions reviewed and resolved/established ✓ Diagnostic scope agreed ✓ Work programme approved ✓ Sponsor acknowledgement signed ✓ Onboarding report approved ✓ Project register updated ✓ Project authorised to proceed, conditionally proceed, return for corrective action, deferred or placed on hold
